Well Information

Date September 5, 1969

Driller Vic Soukup

Test hole No. 69-1 Well location (attach map) South of office in corner

Completed ..... No of man hours as charged to job on time sheet .....

5. MATERIAL:	LENGTH	DIA.	GAUGE OR WALL THICKNESS	MATERIAL	TYPE	NO. OF OPENINGS
6. Screen	50'	12"	Cal.	Stainless Steel	Shutter	
7. Inner Casing	97'	12"	3/8"	Black Pipe		T & C
8. Outer Casing						

9. 20 ~~XXX~~ Yds. of gravel used in the well. Size Half concrete mix, half road gravel

10. Test of well. Did you use test or permanent pump? Test 10" Size of Bowl 7 Stages

11. Size of orifice ..... inch by ..... inch. Orifice tube reading ..... inches.

12. Pumping test — measurements from ground level:

TIME	G.P.M.	STATIC	DRAWDOWN	PUMPING LEVEL
3 Hrs.	644	35'4"	6'	41'8"

13. Recovery in 5 minutes Full, in 30 minutes .....

14. Did you seal bottom of well? Yes. Thickness 1/4 inches, material stainless steel plate.

15. Well underreamed? ..... From ..... feet to ..... feet, ... feet to ..... feet.

16. If all screen was not placed at bottom, state how it was spaced.

From ..... feet to ..... feet; from ..... feet to ..... feet; from ..... feet to ..... feet.

17. Depth of well from ground level to top of plug 145' Size of drilled hole 26"

18. Was cement placed around or between any of the casings? No

19. If so, state where, how much and method used. .....

Layne-Western Company, Omaha, Nebraska — Well Information — Page

CONTRACT Mid-States Packing Company — Well No. 1

Log of well from ground level:
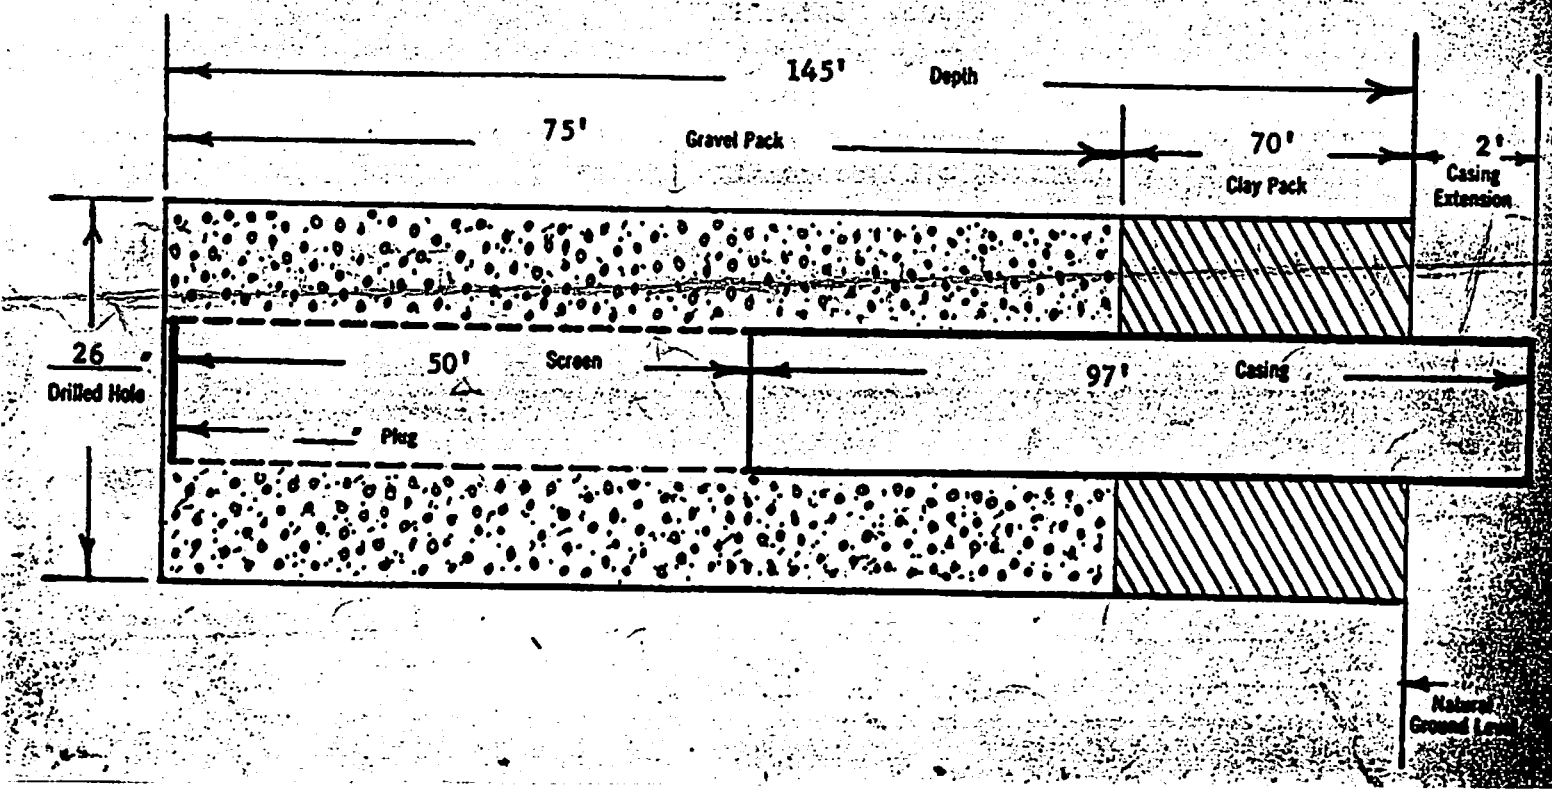
Feet		Feet	Formation
0'	to	4'	Fill.
4'	to	38'	Brown clay.
38'	to	48'	Coarse sand.
48'	to	58'	Blue clay.
58'	to	63'	Coarse sand and gravel.
63'	to	66'	Brown clay.
66'	to	120'	Coarse sand, gravel, fine sand.
120'	to	145'	Coarse sand and gravel.
	to		
	to		
	to		
	to		
	to		
	to		
	to		
	to
